



Regional Class Research Vessel (RCRV)

Status of Construction



UNOLS Annual Meeting
November 21, 2019
Brian Midson, RCRV Program Officer



Project Overview

Three Regional Class Research Vessels (RCRVs) are under construction at Gulf Island Shipyards in Houma, LA



*RV
Taani*



*RV
Resolution*



*RV
Embargoed*



Financial Status

Total Project Cost	\$354 million
Contingency	\$56 million
Completion	19%
Progress Cost	99% of expected
Schedule Performance	92% of expected
Confidence	>90%





Schedule Summary

	2017	2018	2019	2020	2021	2022	2023	2024
R/V Taani		CONSTRUCTION Keel Laying ♦ Nov 2018			Launch ♦ Nov 2020	Delivery ♦ Aug 2021	SEA TRIALS Begin Operations ♦ Aug 2022	
R/V Resolution		CONSTRUCTION Keel Laying ♦ May 2019			Launch ♦ May 2021	Delivery ♦ Feb 2022	SEA TRIALS Begin Operations ♦ Feb 2023	
RCRV 3			CONSTRUCTION Keel Laying ♦ Mar 2020			Launch ♦ Oct 2021	Delivery ♦ Jul 2022	SEA TRIALS Begin Operations ♦ Jul 2023



Module 21, Bulbous Bow





Module 22 Shell Plate installation






Shipyard Webcam

<http://webcam.oregonstate.edu/rcrv3>

RCRV Taani - Cam 3 2019-10-03 05:00:47 CT

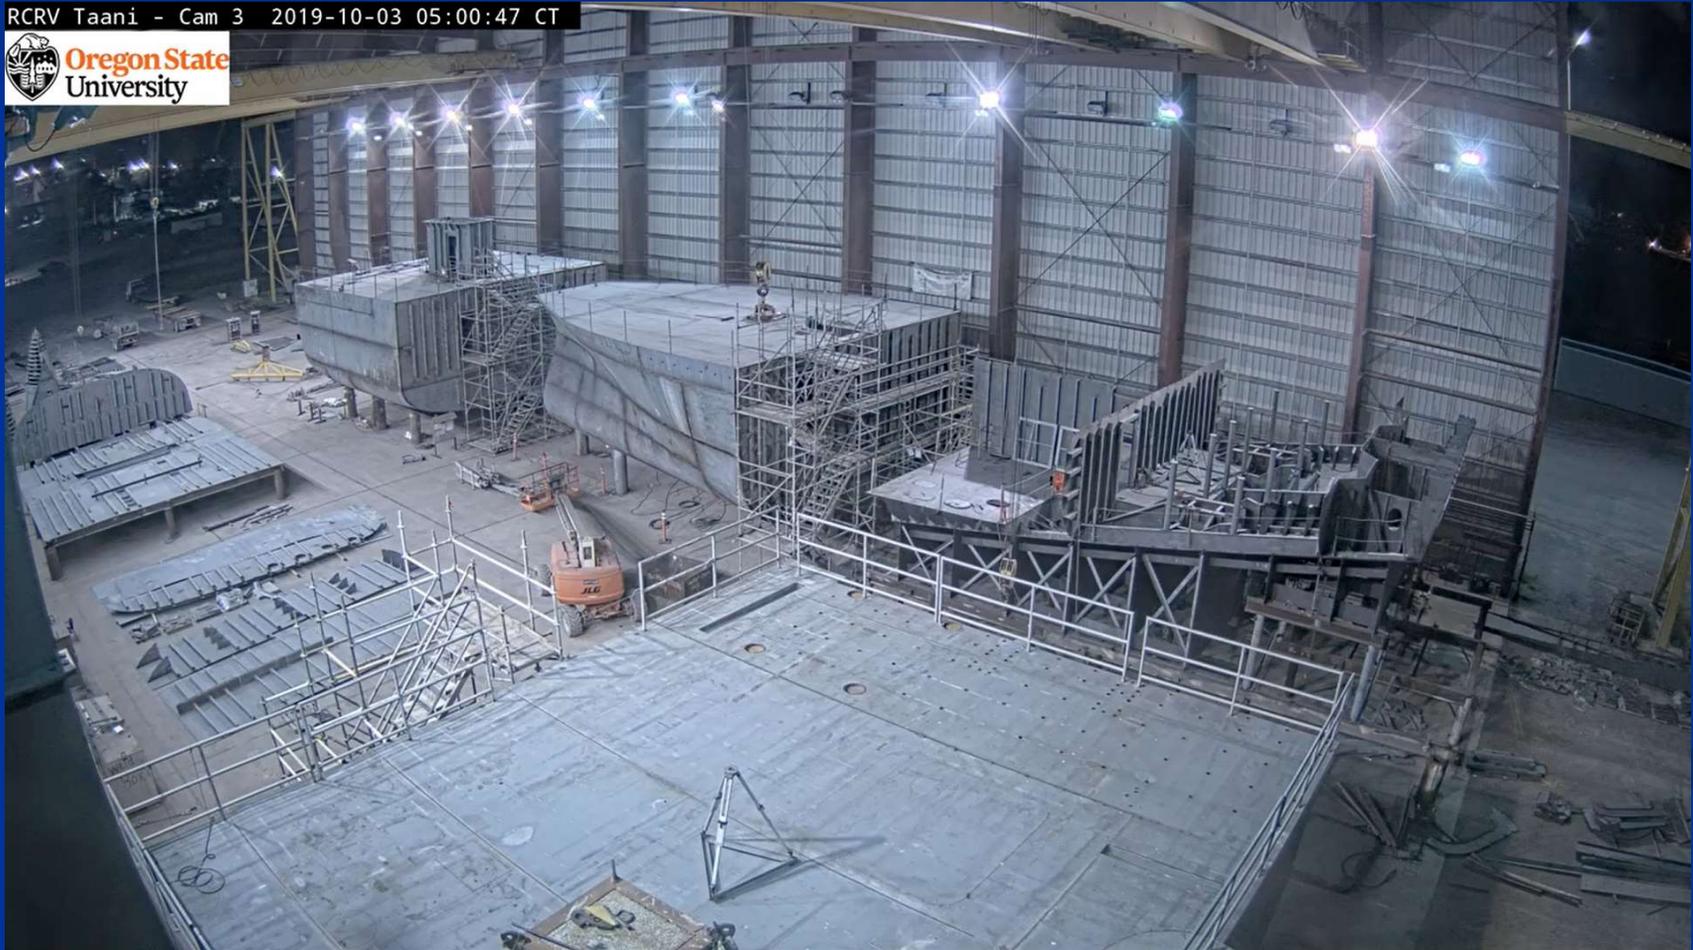



Thank you

Questions?
