



Landseth Shakedown Schedule

task	at-sea Days	start date, time	end date, time	OOS days
transit from Galveston	0.5	6/22/07 0:00	6/22/07 12:00	
unspool & rewind Source umbilicals	0.5	6/22/07 12:00	6/23/07 0:00	
Unspool & rewind Streamers	2	6/23/07 0:00	6/25/07 0:00	
Rig on baro 16 paravanes	0.25	6/25/07 0:00	6/25/07 6:00	
Unspool vane cables with paravanes & rewind	0.5	6/25/07 6:00	6/25/07 18:00	
Deploy, ballast, recover first hydrophone cable	2	6/25/07 18:00	6/27/07 18:00	
redeploy paravanes	0.5	6/27/07 18:00	6/28/07 6:00	
deploy, ballast & adjust 4 hydrophone cables	4	6/28/07 6:00	7/2/07 6:00	
Recover hydrophone cables, paravanes	1.5	7/2/07 6:00	7/3/07 18:00	
Deploy single source string, test controller	0.5	7/3/07 18:00	7/4/07 6:00	
Deploy 3 additional source strings, 2D mode, test fire	1	7/4/07 6:00	7/5/07 6:00	
Recover source strings, redeploy paravanes	0.5	7/5/07 6:00	7/5/07 18:00	
deploy 4 source strings, adjust in 3D mode, test fire	1	7/5/07 18:00	7/6/07 18:00	
Recover gear, transit to port	1	7/6/07 18:00	7/7/07 18:00	
in-port		7/7/07 18:00	7/10/07 18:00	3
Depart Port with BBN, transit to deep calibration site	1	7/10/07 18:00	7/11/07 18:00	
Deploy Calibration instrumentation, CTD, XBT	1	7/11/07 18:00	7/12/07 18:00	
Perform deep calibration	3	7/12/07 18:00	7/15/07 18:00	
recover calibration instrumentation, CTD, XBT	1	7/15/07 18:00	7/16/07 18:00	
Transit to slope calibration site, redeploy instruments	2	7/16/07 18:00	7/18/07 18:00	
CTD, XBT, perform slope calibration	3	7/18/07 18:00	7/21/07 18:00	
recover instrumentation, transit to port, drop BBN	2	7/21/07 18:00	7/23/07 18:00	
in-port		7/23/07 18:00	7/26/07 18:00	3
depart port, transit to OBS test site	1	7/26/07 18:00	7/27/07 18:00	
Test OBSIP deploy, recover, test CTD rosette deploy	1	7/27/07 18:00	7/28/07 18:00	
Transit to shallow source calibration site	1.5	7/28/07 18:00	7/30/07 6:00	
CTD, XBT, Deploy calibration instrumentation	0.5	7/30/07 6:00	7/30/07 18:00	
Shallow water source calibration	3	7/30/07 18:00	8/2/07 18:00	
CTD, XBT, recover calibration instruments	0.5	8/2/07 18:00	8/3/07 6:00	
transit to seismic test site	2	8/3/07 6:00	8/5/07 6:00	
Deploy for 3D test	3	8/5/07 6:00	8/8/07 6:00	
3D test	5.75	8/8/07 6:00	8/14/07 0:00	
recover & transit to port	2	8/14/07 0:00	8/16/07 0:00	
at sea days	49			

Langseth Shakedown sites

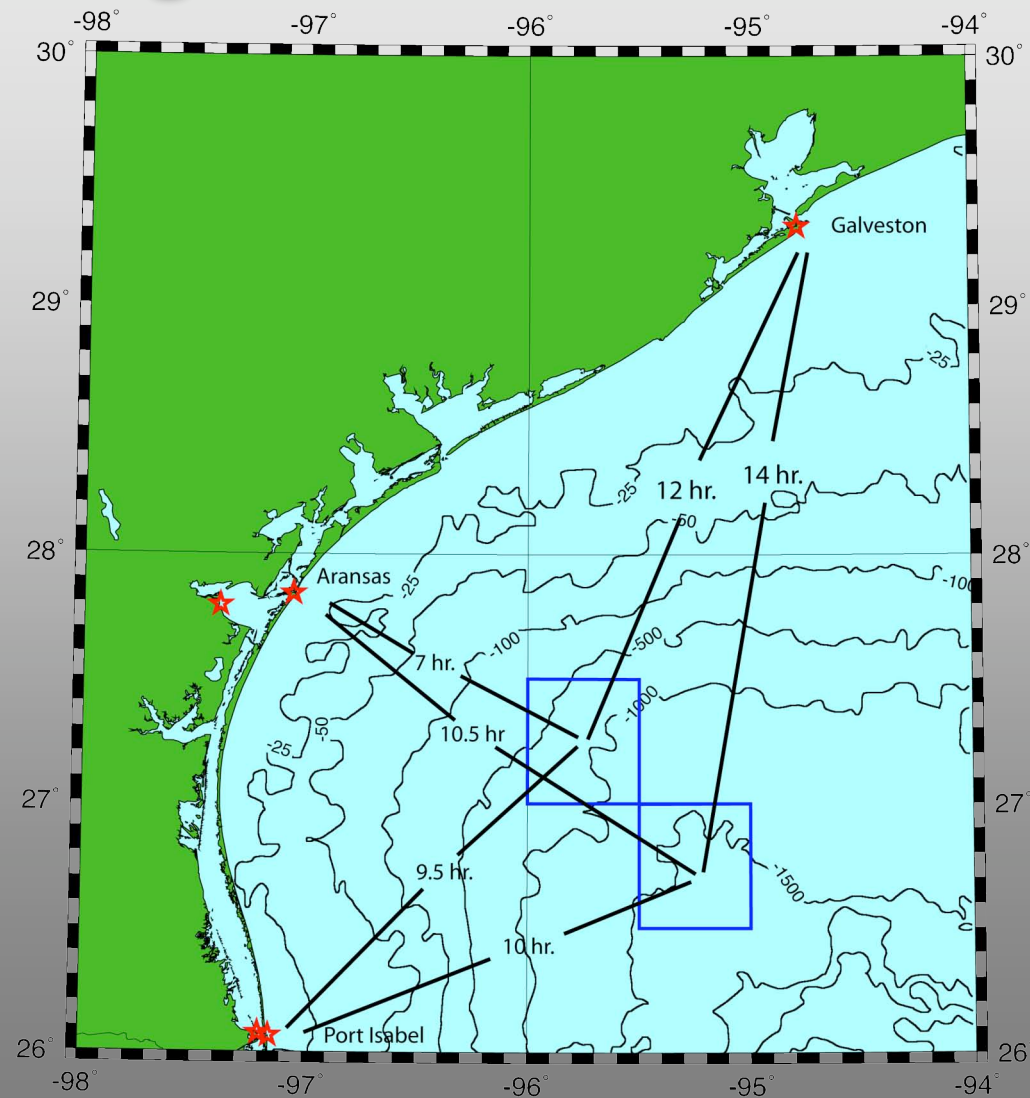

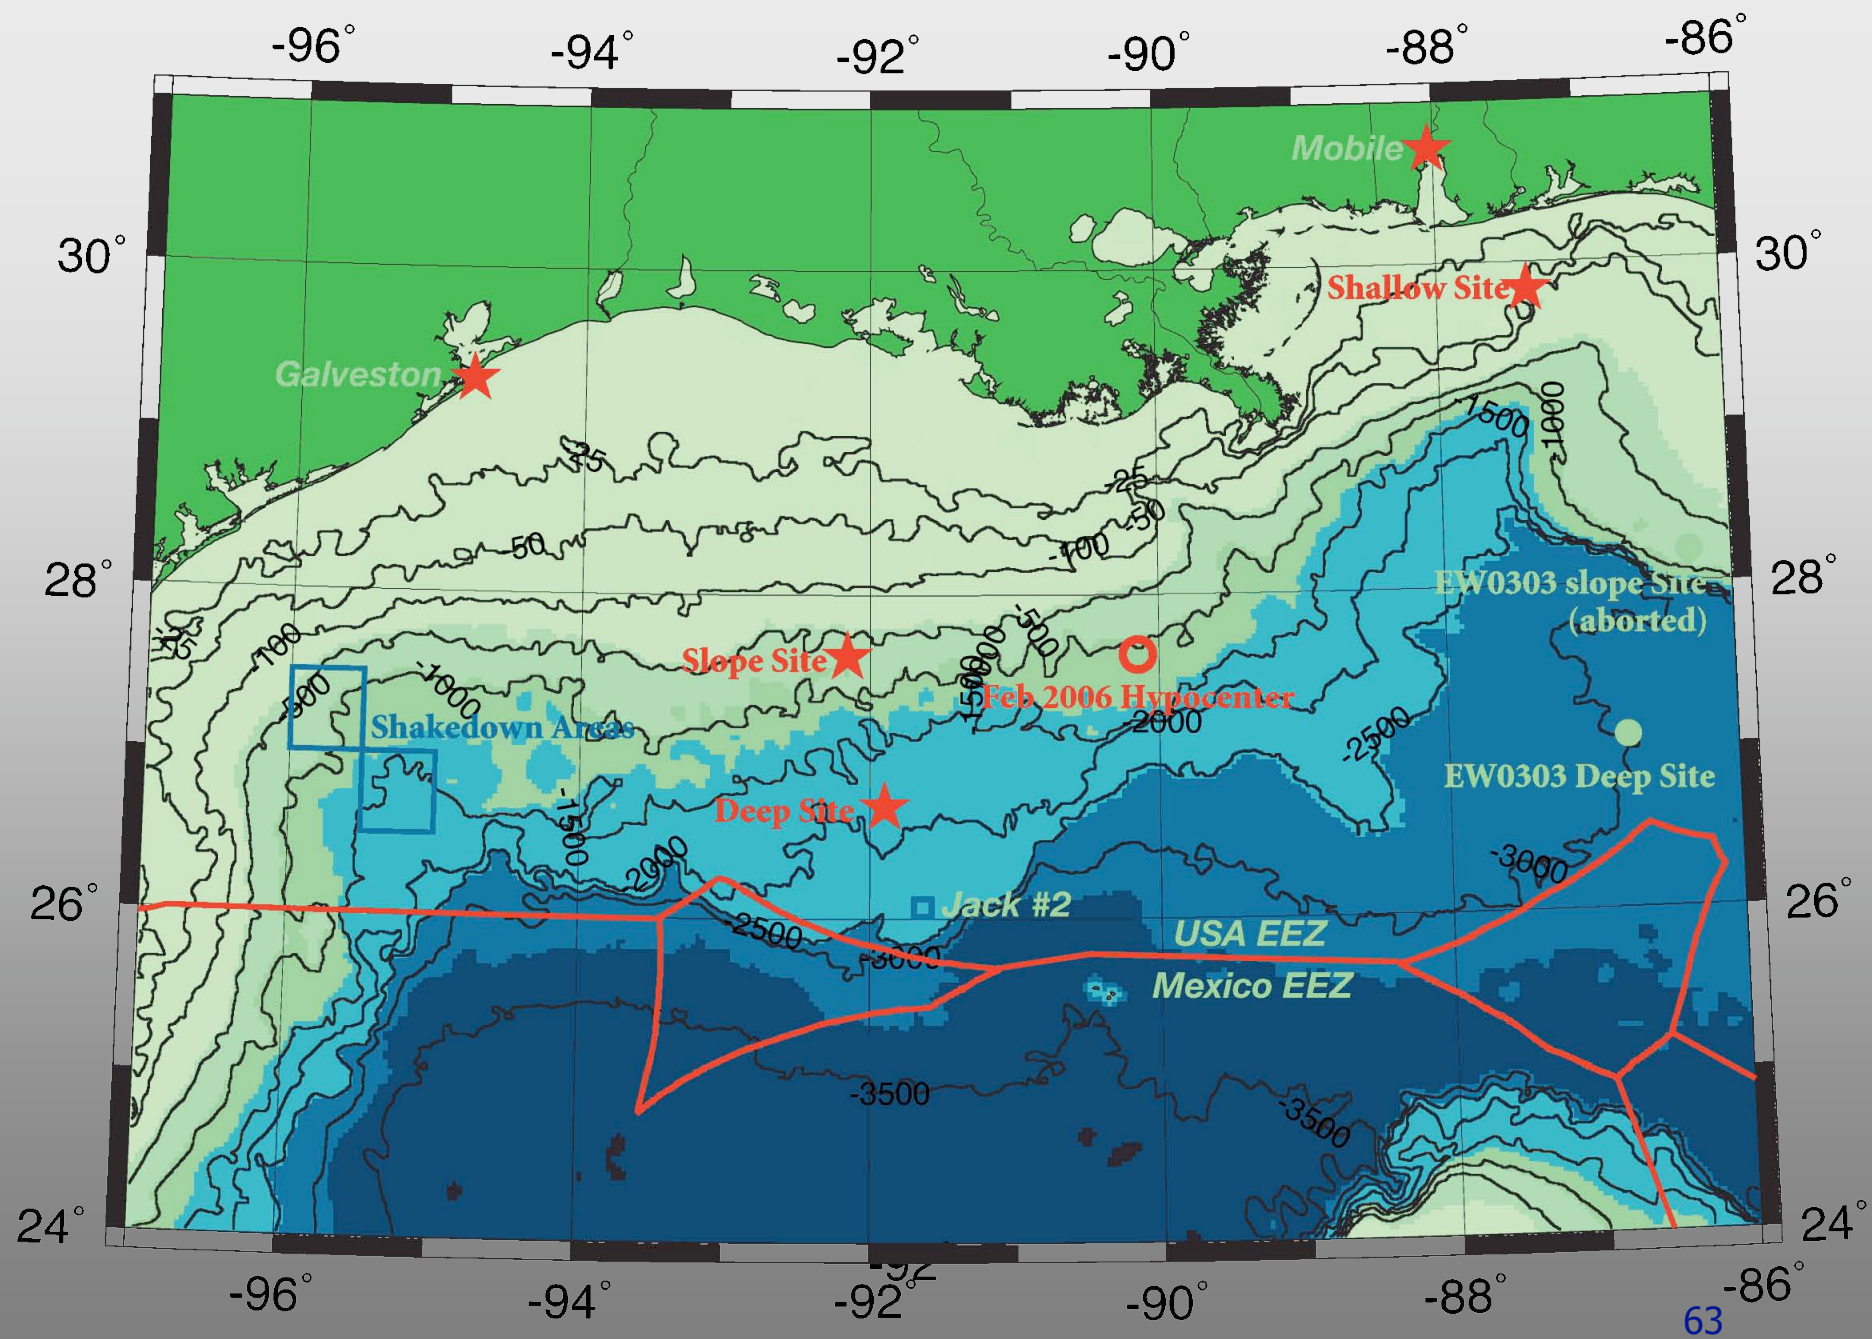

Test Cruise

Who

