



# Ocean Class AGOR Program Acquisition Status

Prepared by PEO Ships, PMS325Q  
For UNOLS Research Vessel Operators Committee  
14 April 2009





# Ocean Class AGOR Agenda

- History/Status of Acquisition Efforts
- History of Specification Development
- Acquisition Schedule
- Proposed UNOLS “At-Large” Representation
- Proposed Operator Representation



## Ocean Class AGOR History of Acquisition Efforts

- ACAT III Designation Letter
  - Signed 14 May 2008
- Acquisition Strategy Report (ASR)
  - Signed 24 Feb 2009
- Agreement with Commander, Operational Test & Evaluation Force
  - Letter signed 15 Dec 2008
- Industry Day
  - Conducted 03 Sep 2008
- Capabilities Development Document (CDD)
  - Signed in 18 Mar 2009
- Source Selection Plan
  - To be signed week of 13 Apr 2009



## Ocean Class AGOR Status of Acquisition Efforts

- Phase I/II Solicitation
  - Release in Apr 2009
  - Proposals due Jun/Jul 2009
  - Phase I: Preliminary/Contract Design
    - Contract awards ~ Aug/Sep 2009
    - Post award conferences ~ Sep/Oct 2009
    - First design reviews ~ Nov/Dec 2009
  - Phase II: Detail Design and Construction
    - Contract award ~ FY 2011, Q2
- Deliveries:
  - 1<sup>st</sup> ship – FY 2014, Q2
  - 2<sup>nd</sup> ship – FY 2014, Q4




# Ocean Class AGOR History of Specification Development

- Ocean Class Science Mission Requirements
  - Version 1.1, issued Aug 2007
- Attachment J-1, System Specification
  - Version 1.3, issued 14 Jan 2009
- Attachment J-6, Mission Equipment Specification
  - Version 1.3, issued 14 Jan 2009
- UNOLS Community Input
  - 06 Oct 2008: UNOLS review of System Specification
  - 15-16 Oct 2008: Phonecon reading session with UNOLS reviewers
  - 20-24 Oct 2008: Incorporation of UNOLS comments
- Ocean Class Science Mission Requirements
  - Forthcoming update



# Ocean Class AGOR Acquisition Schedule

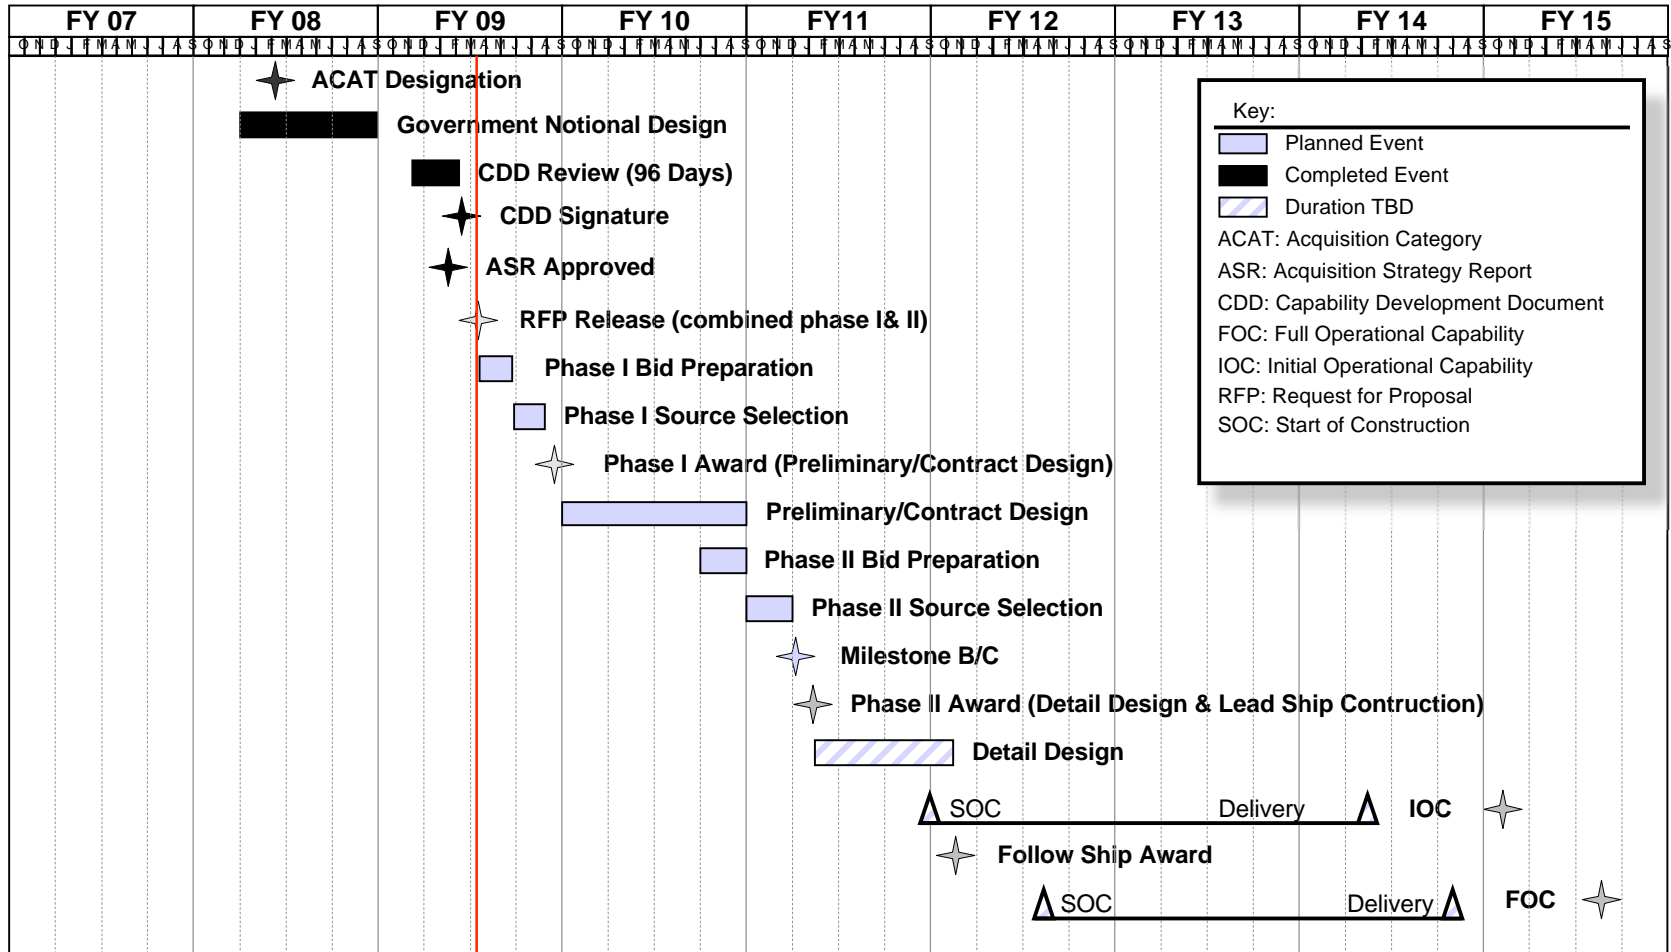



# Ocean Class AGOR Q&A

- Questions?
